

**THE BROADWAY**

**MULTIPLEX**

# Construction Activity

Weekly Look Ahead Report – 03<sup>rd</sup> May to 10<sup>th</sup> May 2019



For any queries or further information please contact:

**Broadway Community Team**

24 hour phone line: +44 (0)79 1278 3844

community@multiplex.global

[www.tenbroadway.com](http://www.tenbroadway.com)

**B**

**THE BROADWAY**

WESTMINSTER

## Construction Activity

### Weekly Look Ahead Report – 03<sup>rd</sup> May to 10<sup>th</sup> May 2019


#### Weekend Works

##### Saturday 04<sup>th</sup> May 2019


- Erecting of mast sections, slew ring, counter jib and A-Frame. Front jib will be unloaded and assembled by the mobile crane on the Broadway.
- The test weights as well as the last 2 sections of front jib will be unloaded and assembled by TC1A.

##### Sunday 05<sup>th</sup> May 2019

- Jib sections to be erected by the mobile crane and TC1A, install last of counterweights and load tests to be carried out.

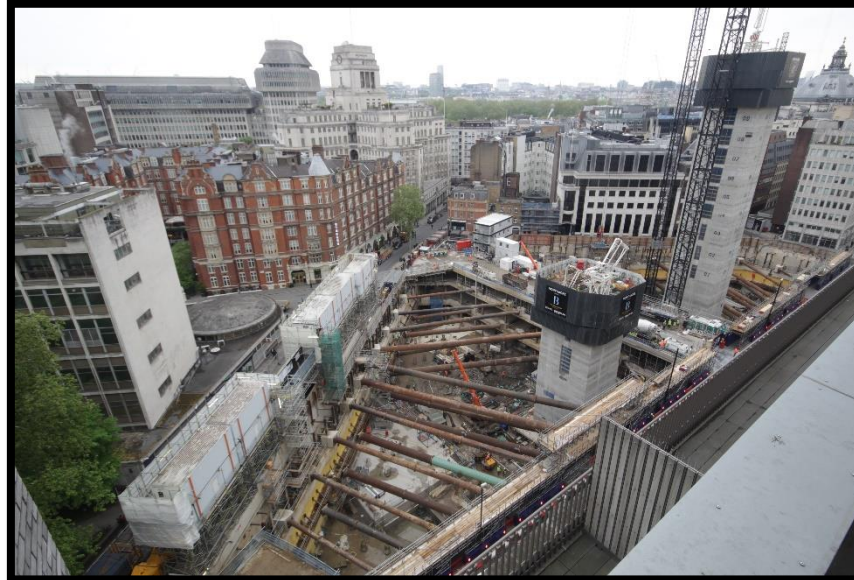

Site Eye

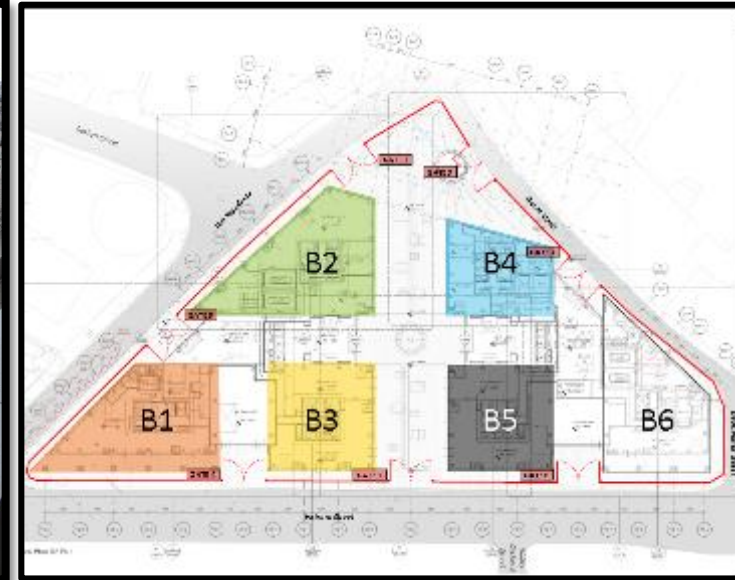

Building number – Plan layout

For any queries or further information please contact:

**Broadway Community Team**

24 hour phone line: +44 (0)79 1278 3844

community@multiplex.global

[www.tenbroadway.com](http://www.tenbroadway.com)



## THE BROADWAY

WESTMINSTER


## Construction Activity

### Weekly Look Ahead Report – 03<sup>rd</sup> May to 10<sup>th</sup> May 2019


#### Works to be carried out in the coming week:

#### Monday 06<sup>th</sup> May to Friday 10<sup>th</sup> May

- Working hours – 08:00 to 18:00
- Dispensation:
  - to start excavation at 07:30
  - To unload deliveries till 19:00
- Erection of scaffold bridges across gates on Victoria Street
- No works on Monday
- Large concrete pours to site will take place on the following days (power floating will take place overnight)
  - Wednesday 08<sup>th</sup> May
  - Thursday 9<sup>th</sup> May
  - Friday 10<sup>th</sup> May
- Rebar fixing to building B4 basement level 2
- Concrete to slipform on Cores 3 and 5
- Construction of building B5 and B6 columns and liner walls

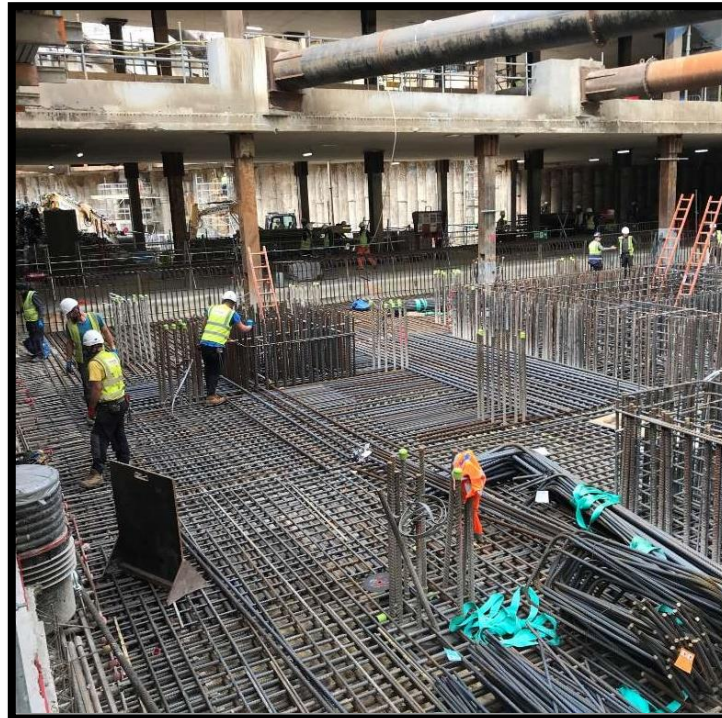

East – Rebar for concrete pour of Basement Level 2

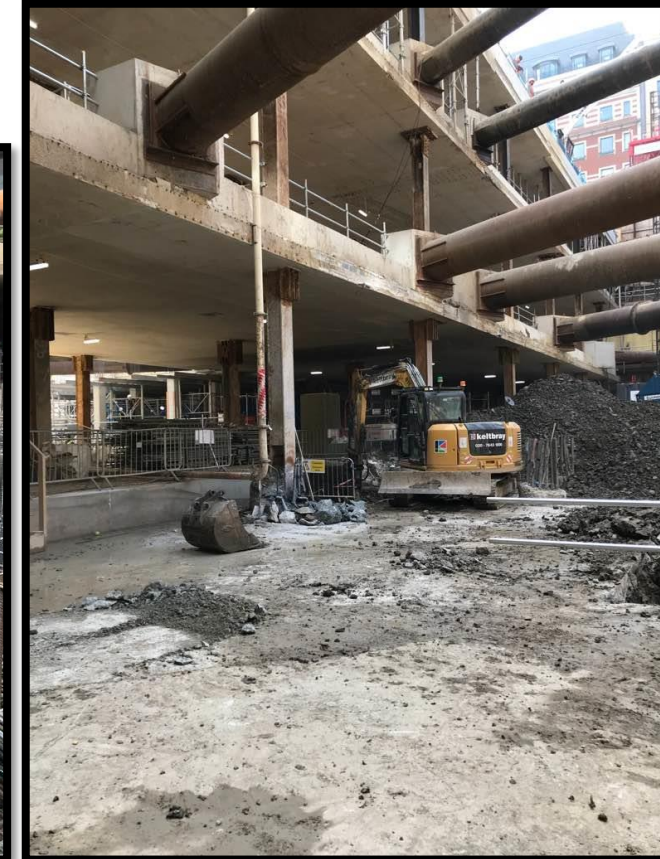

West - Excavation & Piling completed and demobilised from site

For any queries or further information please contact:

**Broadway Community Team**


24 hour phone line: +44 (0)79 1278 3844

community@multiplex.global

[www.tenbroadway.com](http://www.tenbroadway.com)

# THE BROADWAY

WESTMINSTER



THE BROADWAY

WESTMINSTER

**MULTIPLEX**

For any queries or further information please contact:

**Broadway Community Team**

24 hour phone line: +44 (0)79 1278

3844 [community@multiplex.global](mailto:community@multiplex.global)

[www.tenbroadway.com](http://www.tenbroadway.com)
